

# LAKE WORTH TRAIL

## Project Update

June 28, 2018

Lake Worth Regional Coordination Committee Meeting

City of Fort Worth  
Park & Recreation Department

## Master Plan

( September 2015)

- Lake Worth Gas Lease Capital Projects Fund



## Phase 1 Project Outline

- Budget: \$7,347,234
- Approx. 5.5 miles
- Challenges
  - Topography
  - Soil Condition
  - Easements
  - Narrow ROW
  - Budget

## Current Status

- Redesigning New Alignment



**Current Alignment**

**Green:** Same with previous Off-street

**Yellow:** **NEW:** Off-street

**Blue:** **NEW:** On-street

**Previous Alignments**

**Red:** Abandoned due to Soil Failure

**Purple:** Reported as being studied in June, 2017





**Marion  
Sansom  
Park**

**Off-street  
Alignment**

**ENLARGEMENT**



Conceptual  
Off-street  
Alignment


Marion Sansom Park

0 1,000 2,000 Feet

0 0.25 0.5 Miles

**ENLARGEMENT**



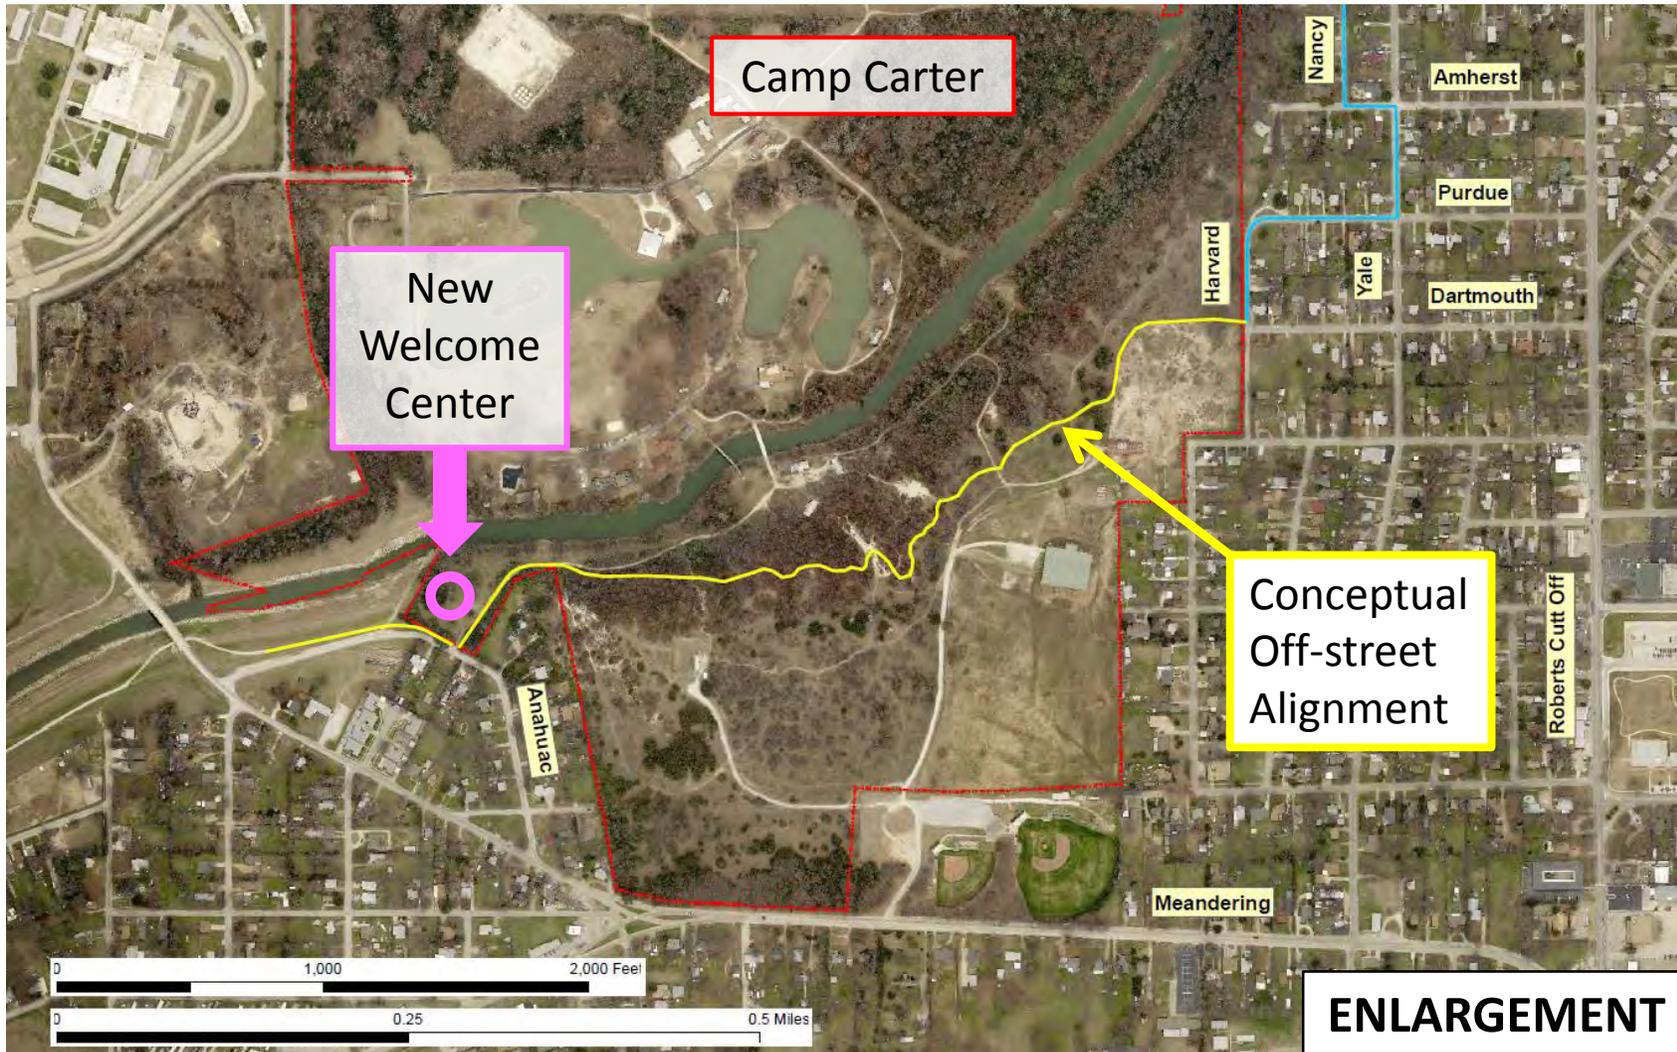



# Schedule

- Design
  - Complete Widening (10 FT wide)  
of Western Segment: August 2018
  - Alignment Study of Eastern Segment: Late Summer 2018
  
- Construction
  - Western Segment: Starts in Late Summer 2018
  - Eastern Segment: Starts in Mid 2019

# Lake Worth Trail

## Contact:

Naoto Kumazawa, Landscape Architect

[Naoto.Kumazawa@fortworthtexas.gov](mailto:Naoto.Kumazawa@fortworthtexas.gov)

817-392-5742



# LOVE CIRCLE PARK IMPROVEMENTS

## Project Update

June 28, 2018

Lake Worth Regional Coordination Committee Meeting

City of Fort Worth  
Park & Recreation Department

## Project Outline

- Budget: \$200,000.  
(Lake Worth Gas Lease Capital Projects Fund)
- Mayor & Council Approved on Feb 6, 2018
- 6 FT wide Tail approx. 0.9 mile long

## Current Status

- Approx. 50% Completion
- Schedule to Complete in August 2018

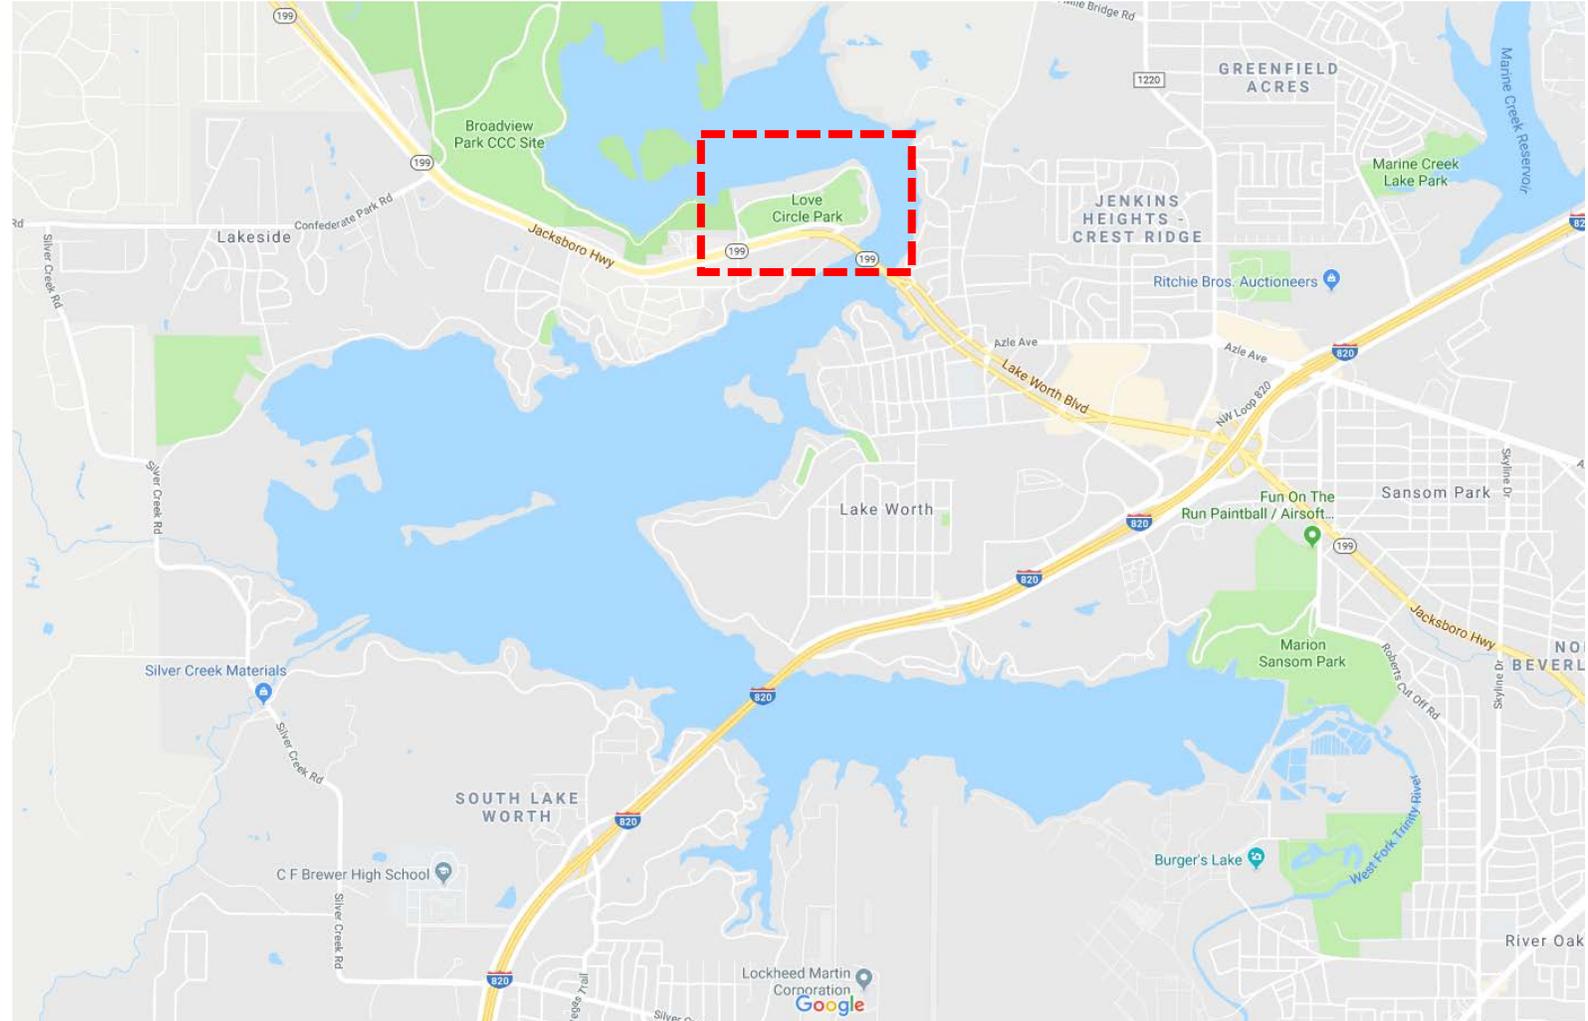






Photo: June 25, 2018

# Love Circle Park Improvements

## Contact:

Scott Penn, District Superintendent

[Scott.Penn@fortworthtexas.gov](mailto:Scott.Penn@fortworthtexas.gov)

817-392-5750
