


# Cromwell Marine Creek Road Construction

## September 2026 Update

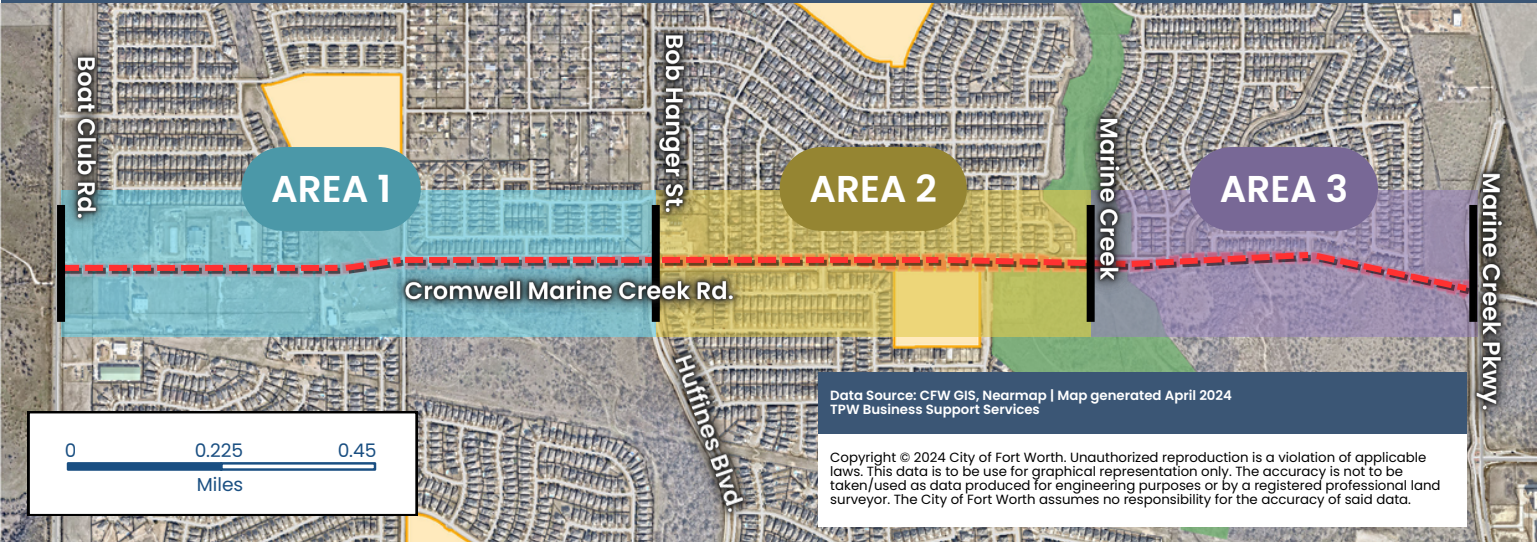

**Sundt Construction, Inc. is currently working in the following areas:**

The City is diligently working with the contractor, Sundt Construction, to **expedite the completion** of the project to open the newly completed Cromwell Marine Creek Road pavement by November 2026.

● **Area 1**

**Boat Club Rd. to Huffines/Bob Hanger Rd.**

All travel lane pavement has been completed. Remaining work before opening the lanes:

- *Striping of lanes, signage and street illumination*
- *Traffic signal installation at the intersections of Boat Club Road, Bowman Roberts and Bob Hanger/Huffines – starting the week of September 8, 2026*

● **Area 2**

**Huffines/Bob Hanger St. to Marine Creek**

Sundt has completed all westbound pavement between Huffines/Bob Hanger and the Marine Creek bridge. Remaining work to be completed:

- *Huffines/Bob Hanger intersection improvements*
- *Eastbound turn lanes from Huffines/Bob Hanger to Crystal Lake/Provinces*
- *Sidewalks, striping of lanes, signage and street illumination and signal at Crystal Lake*

● **Area 3**

**Marine Creek to Marine Creek Pkwy. Roundabout**

All travel lane pavement is complete. Opening of traffic is pending completion of the intersection at Crystal Lake and the roundabout western island as well as striping. Completion is anticipated by November 2026. Remaining work to be completed:

- *Sidewalks, handicap ramps & retaining walls at Bay Lake*
- *Striping of lanes, signage and street illumination*

### COMPLETION TIMELINE

*As of September 2026*

| LOCATION                                                 | EST. COMPLETION<br><i>Weather Permitting</i> |
|----------------------------------------------------------|----------------------------------------------|
| ● <b>AREA 1</b>                                          | <b>NOV. 2026</b>                             |
| ● <b>AREA 2</b>                                          | <b>DEC. 2026</b>                             |
| ● <b>AREA 3</b>                                          | <b>DEC. 2026</b>                             |
| CRYSTAL LAKE DRIVE AND TRAFFIC SIGNAL                    | NOV. 2026                                    |
| NEPTUNE ST.                                              | NOV. 2026 <b>COMPLETE</b>                    |
| MARITIME ST.                                             | NOV. 2026 <b>COMPLETE</b>                    |
| PROVINCES ST.                                            | DEC. 2026 <b>COMPLETE</b>                    |
| BRITANNIC ST.                                            | DEC. 2026 <b>COMPLETE</b>                    |
| CAPE ST.                                                 | NOV. 2026 <b>COMPLETE</b>                    |
| BAY LAKE DR.                                             | NOV. 2026                                    |
| CROMWELL MARINE CREEK RD. /MARINE CREEK PKWY. ROUNDABOUT | NOV. 2026                                    |

CONNECT WITH US.



**Get Connected. Stay Informed.**

To subscribe to projects updates and receive more information about capital projects, visit [fortworthtexas.gov](https://fortworthtexas.gov)
